


POPLAR GROVE CHILD DEVELOPMENT CENTER  
 PLANNING STUDY PRELIMINARY SCHEDULE  
 SEPTEMBER 13, 2018

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Timeline											
							Sep	Qtr 4, 2018	Oct	Nov	Dec	Qtr 1, 2019	Jan	Feb	Mar	Qtr 2, 2019	Apr	May
1		<b>PLANNING SELECTION</b>	<b>48 days</b>	<b>Wed 9/12/18</b>	<b>Mon 11/19/18</b>													
2		Feasibility Study Consultant Advertisement	18 days	Wed 9/12/18	Fri 10/5/18													
3		Baseline Information Assembly	28 days	Wed 9/12/18	Fri 10/19/18	2SS												
4		Short Listing	10 days	Mon 10/8/18	Fri 10/19/18	2												
5		Short List Notifications	0 days	Mon 10/22/18	Mon 10/22/18													
6		Presentation Preparation	10 days	Mon 10/22/18	Fri 11/2/18	5,3												
7		Presentations	5 days	Mon 11/5/18	Fri 11/9/18	6												
8		Deliberations,Evaluations & Grading	5 days	Mon 11/12/18	Fri 11/16/18	7												
9		Notification of Award and Thankyou's	0 days	Mon 11/19/18	Mon 11/19/18													
10		<b>PLANNING CONTRACTING</b>	<b>46 days</b>	<b>Mon 11/19/18</b>	<b>Mon 1/21/19</b>													
11		Planning Scoping Meeting	1 day	Mon 11/19/18	Mon 11/19/18	9												
12		Fee Proposal Preparation	15 days	Tue 11/20/18	Mon 12/10/18	11												
13		Fee Proposal Review	5 days	Tue 12/11/18	Mon 12/17/18	12												
14		Preparation of Letter Agreement	15 days	Tue 12/18/18	Mon 1/7/19	13												
15		Issuance of Letter Agreement	0 days	Tue 1/8/19	Tue 1/8/19	14												
16		Execution of Planning Agreement	10 days	Tue 1/8/19	Mon 1/21/19	15												
17		<b>PLANNING</b>	<b>89 days</b>	<b>Tue 1/22/19</b>	<b>Fri 5/24/19</b>													
18		Initial Planning & Data Collection	30 days	Tue 1/22/19	Mon 3/4/19	16												
19		Initial Presentation	1 day	Tue 3/5/19	Tue 3/5/19	18												
20		Preparation of Alternatives	30 days	Wed 3/6/19	Tue 4/16/19	19												
21		Presentation of Alternatives	1 day	Wed 4/17/19	Wed 4/17/19	20												
22		Evaluation of Alternatives	5 days	Thu 4/18/19	Wed 4/24/19	21												
23		Acceptance of Alternatives for Final Report	1 day	Thu 4/25/19	Thu 4/25/19	22												
24		Preparation of Final Report & Presentations	15 days	Fri 4/26/19	Thu 5/16/19	23												
25		Presentation of Final Report	1 day	Fri 5/17/19	Fri 5/17/19	24												
26		Publication of Final Report to Leadership	5 days	Mon 5/20/19	Fri 5/24/19	25												
27																		
28																		
29																		

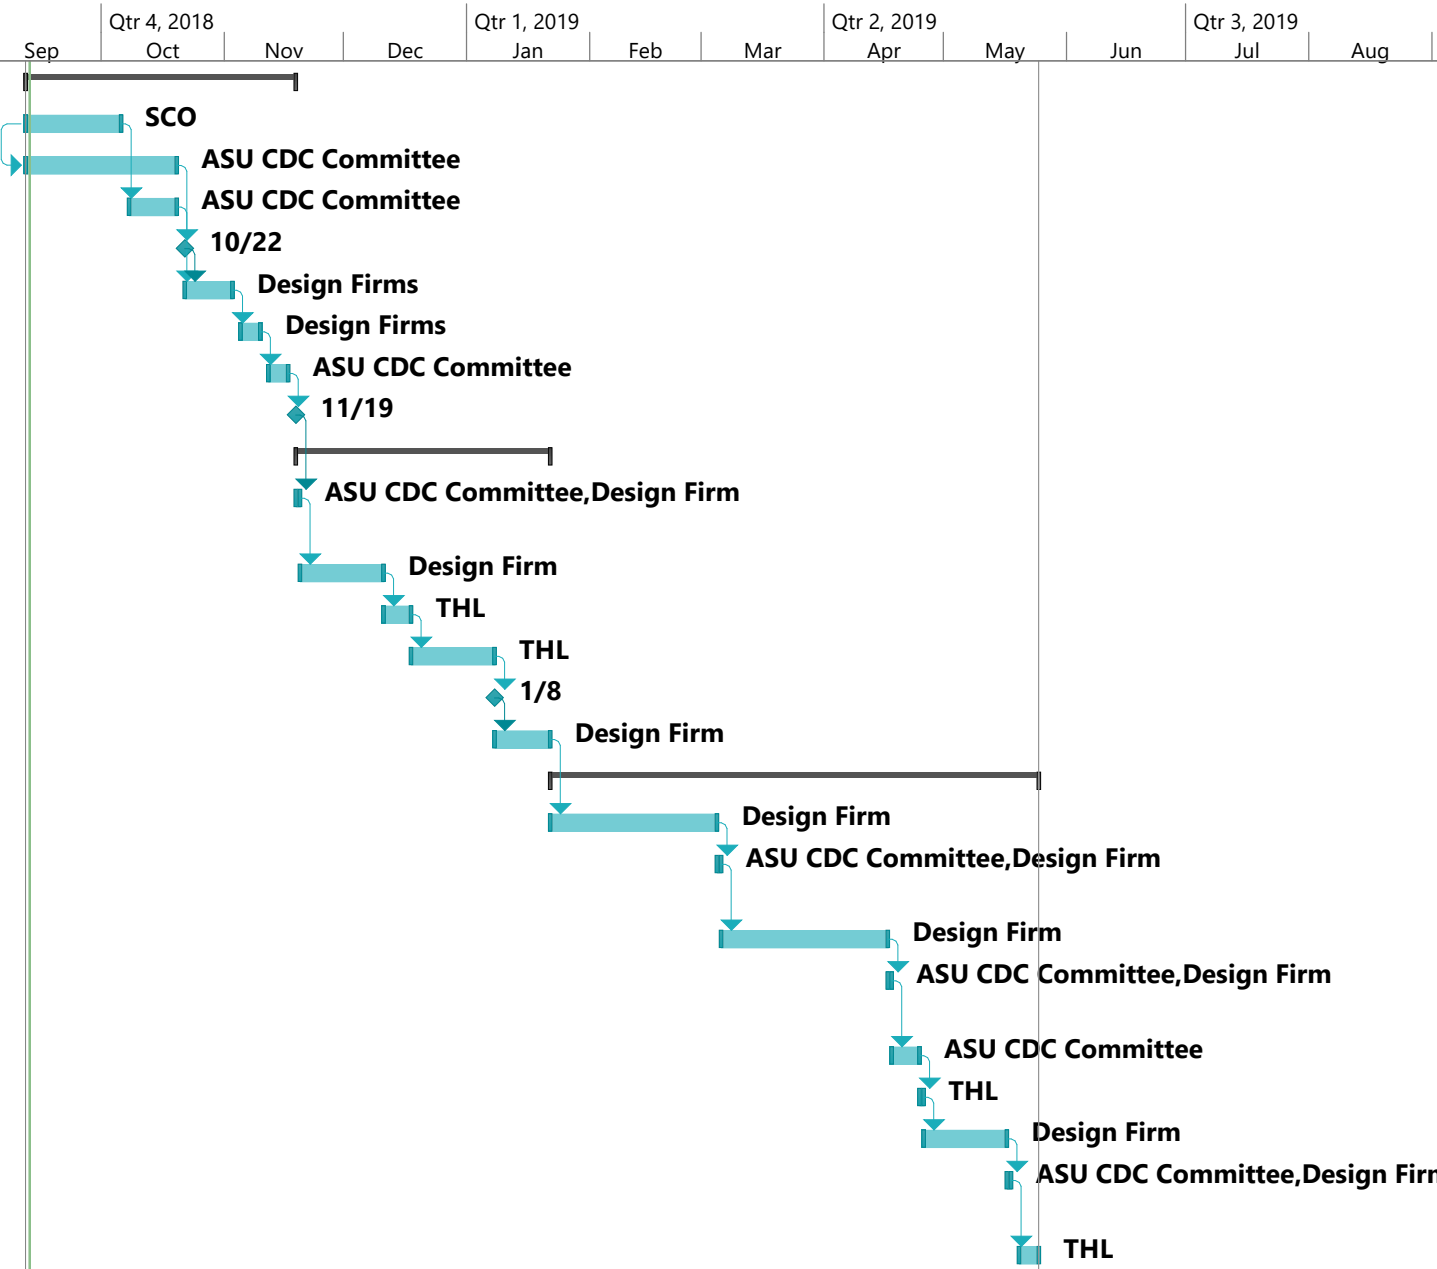

Project: 180913 Poplar Grove C  
Date: Thu 9/13/18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
